



ID	Task Name	Duration	Start	Finish	Predecessors	Mar '22	Apr '22	May '22	Jun '22	Jul '22	Aug '22																			
0	<b>Schematic Design - Schedule - Assignment 5</b>	<b>72 days</b>	<b>Mon 5/2/22</b>	<b>Tue 8/9/22</b>		27	6	13	20	27	3	10	17	24	1	8	15	22	29	5	12	19	26	3	10	17	24	31	7	14
1	<b>1 Habitat for Humanity</b>	<b>72 days</b>	<b>Mon 5/2/22</b>	<b>Tue 8/9/22</b>																										
2	<b>1.1 Design &amp; Permitting</b>	<b>14 days</b>	<b>Mon 5/2/22</b>	<b>Thu 5/19/22</b>																										
3	1.1.1 Construction Design	10 days	Mon 5/2/22	Fri 5/13/22																										
4	1.1.2 Construction Fees	1 day	Tue 5/10/22	Tue 5/10/22	3SS+6 days																									
5	1.1.3 Architecture Fees	1 day	Tue 5/10/22	Tue 5/10/22	4SS																									
6	1.1.4 Engineering Fees	1 day	Tue 5/10/22	Tue 5/10/22	5SS																									
7	1.1.5 Quality Control	3 days	Wed 5/11/22	Fri 5/13/22	6SS+1 day																									
8	1.1.6 PPE	2 days	Thu 5/12/22	Fri 5/13/22	7SS+1 day																									
9	1.1.7 Insurance	1 day	Wed 5/11/22	Wed 5/11/22	6SS+1 day																									
10	1.1.8 Building Permit	3 days	Wed 5/11/22	Fri 5/13/22	6SS+1 day																									
11	1.1.9 Final Civil Package	4 days	Mon 5/16/22	Thu 5/19/22	3																									
12	<b>1.2 Equipment Arrival</b>	<b>6 days</b>	<b>Wed 6/1/22</b>	<b>Wed 6/8/22</b>																										
13	1.2.1 Boom Truck	1 day	Wed 6/1/22	Wed 6/1/22																										
14	1.2.2 Electrical Equipment	1 day	Wed 6/1/22	Wed 6/1/22																										
15	1.2.3 Plumbing Equipment	1 day	Wed 6/1/22	Wed 6/1/22																										
16	1.2.4 Site Equipment	1 day	Wed 6/1/22	Wed 6/1/22																										
17	1.2.5 Concrete Equipment	1 day	Wed 6/1/22	Wed 6/1/22																										
18	1.2.6 48' Flatbed Trailer	1 day	Wed 6/1/22	Wed 6/1/22																										
19	<b>1.3 Sitework</b>	<b>7 days</b>	<b>Wed 6/1/22</b>	<b>Thu 6/9/22</b>																										
20	1.3.1 Topography Survey	1 day	Thu 6/2/22	Thu 6/2/22	16																									
21	1.3.2 Boundary Survey	1 day	Thu 6/2/22	Thu 6/2/22	20																									
22	1.3.3 Clear and Grub	1 day	Fri 6/3/22	Fri 6/3/22	21																									
23	1.3.4 Excavate and Fill	4 days	Mon 6/6/22	Thu 6/9/22	22SS+1 day																									
24	1.3.5 Temporary Gravel	2 days	Tue 6/7/22	Wed 6/8/22	23SS+1 day																									
25	1.3.6 Temporary Silk Fence	2 days	Tue 6/7/22	Wed 6/8/22	23SS+1 day																									
26	1.3.7 Temporary Power	1 day	Tue 6/7/22	Tue 6/7/22	23SS+1 day																									
27	<b>1.4 Storage Shed</b>	<b>2 days</b>	<b>Fri 6/10/22</b>	<b>Mon 6/13/22</b>																										
28	1.4.1 Foundation	1 day	Fri 6/10/22	Fri 6/10/22	23																									
29	1.4.2 Exterior Framing	1 day	Fri 6/10/22	Fri 6/10/22	28SS																									
30	1.4.3 Roof Framing	1 day	Mon 6/13/22	Mon 6/13/22	28SS+1 day																									
31	1.4.4 Siding	1 day	Fri 6/10/22	Fri 6/10/22	28SS																									
32	1.4.5 Opening	1 day	Fri 6/10/22	Fri 6/10/22	28SS																									
33	1.4.6 Light Fixture	1 day	Mon 6/13/22	Mon 6/13/22	28SS+1 day																									
34	<b>1.5 Road Development</b>	<b>10 days</b>	<b>Wed 6/8/22</b>	<b>Tue 6/21/22</b>																										
35	1.5.1 Sub Grade	2 days	Wed 6/8/22	Thu 6/9/22	26																									

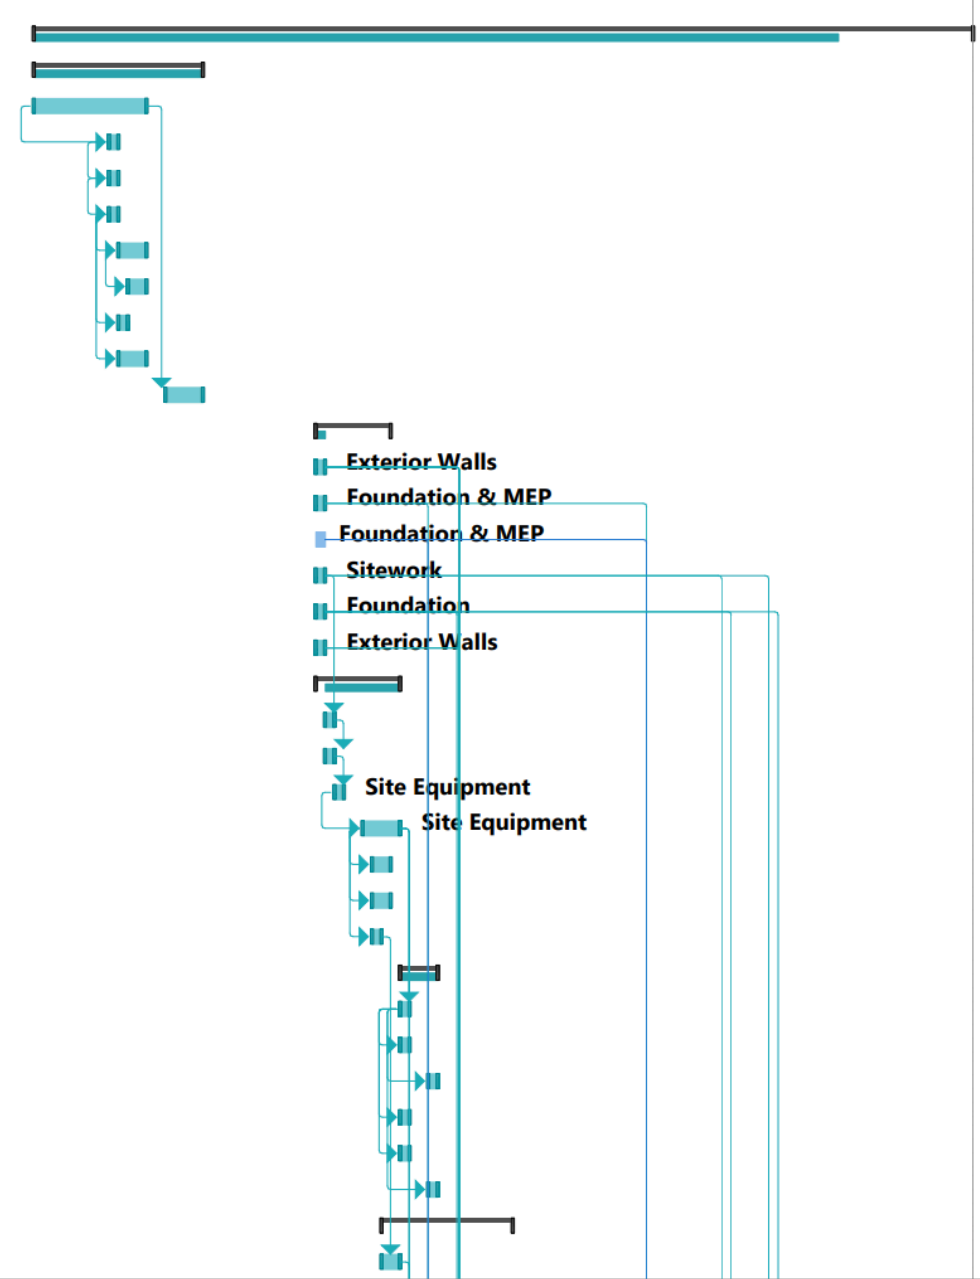


Project: Schematic Design - Sch Date: Tue 4/19/22	Task	Inactive Task	Manual Summary Rollup	External Milestone	Manual Progress
	Split	Inactive Milestone	Manual Summary	Deadline	Critical
	Milestone	Inactive Summary	Start-only	Critical Split	Critical
	Summary	Manual Task	Finish-only	Critical Split	Critical Split
	Project Summary	Duration-only	External Tasks	Progress	Progress

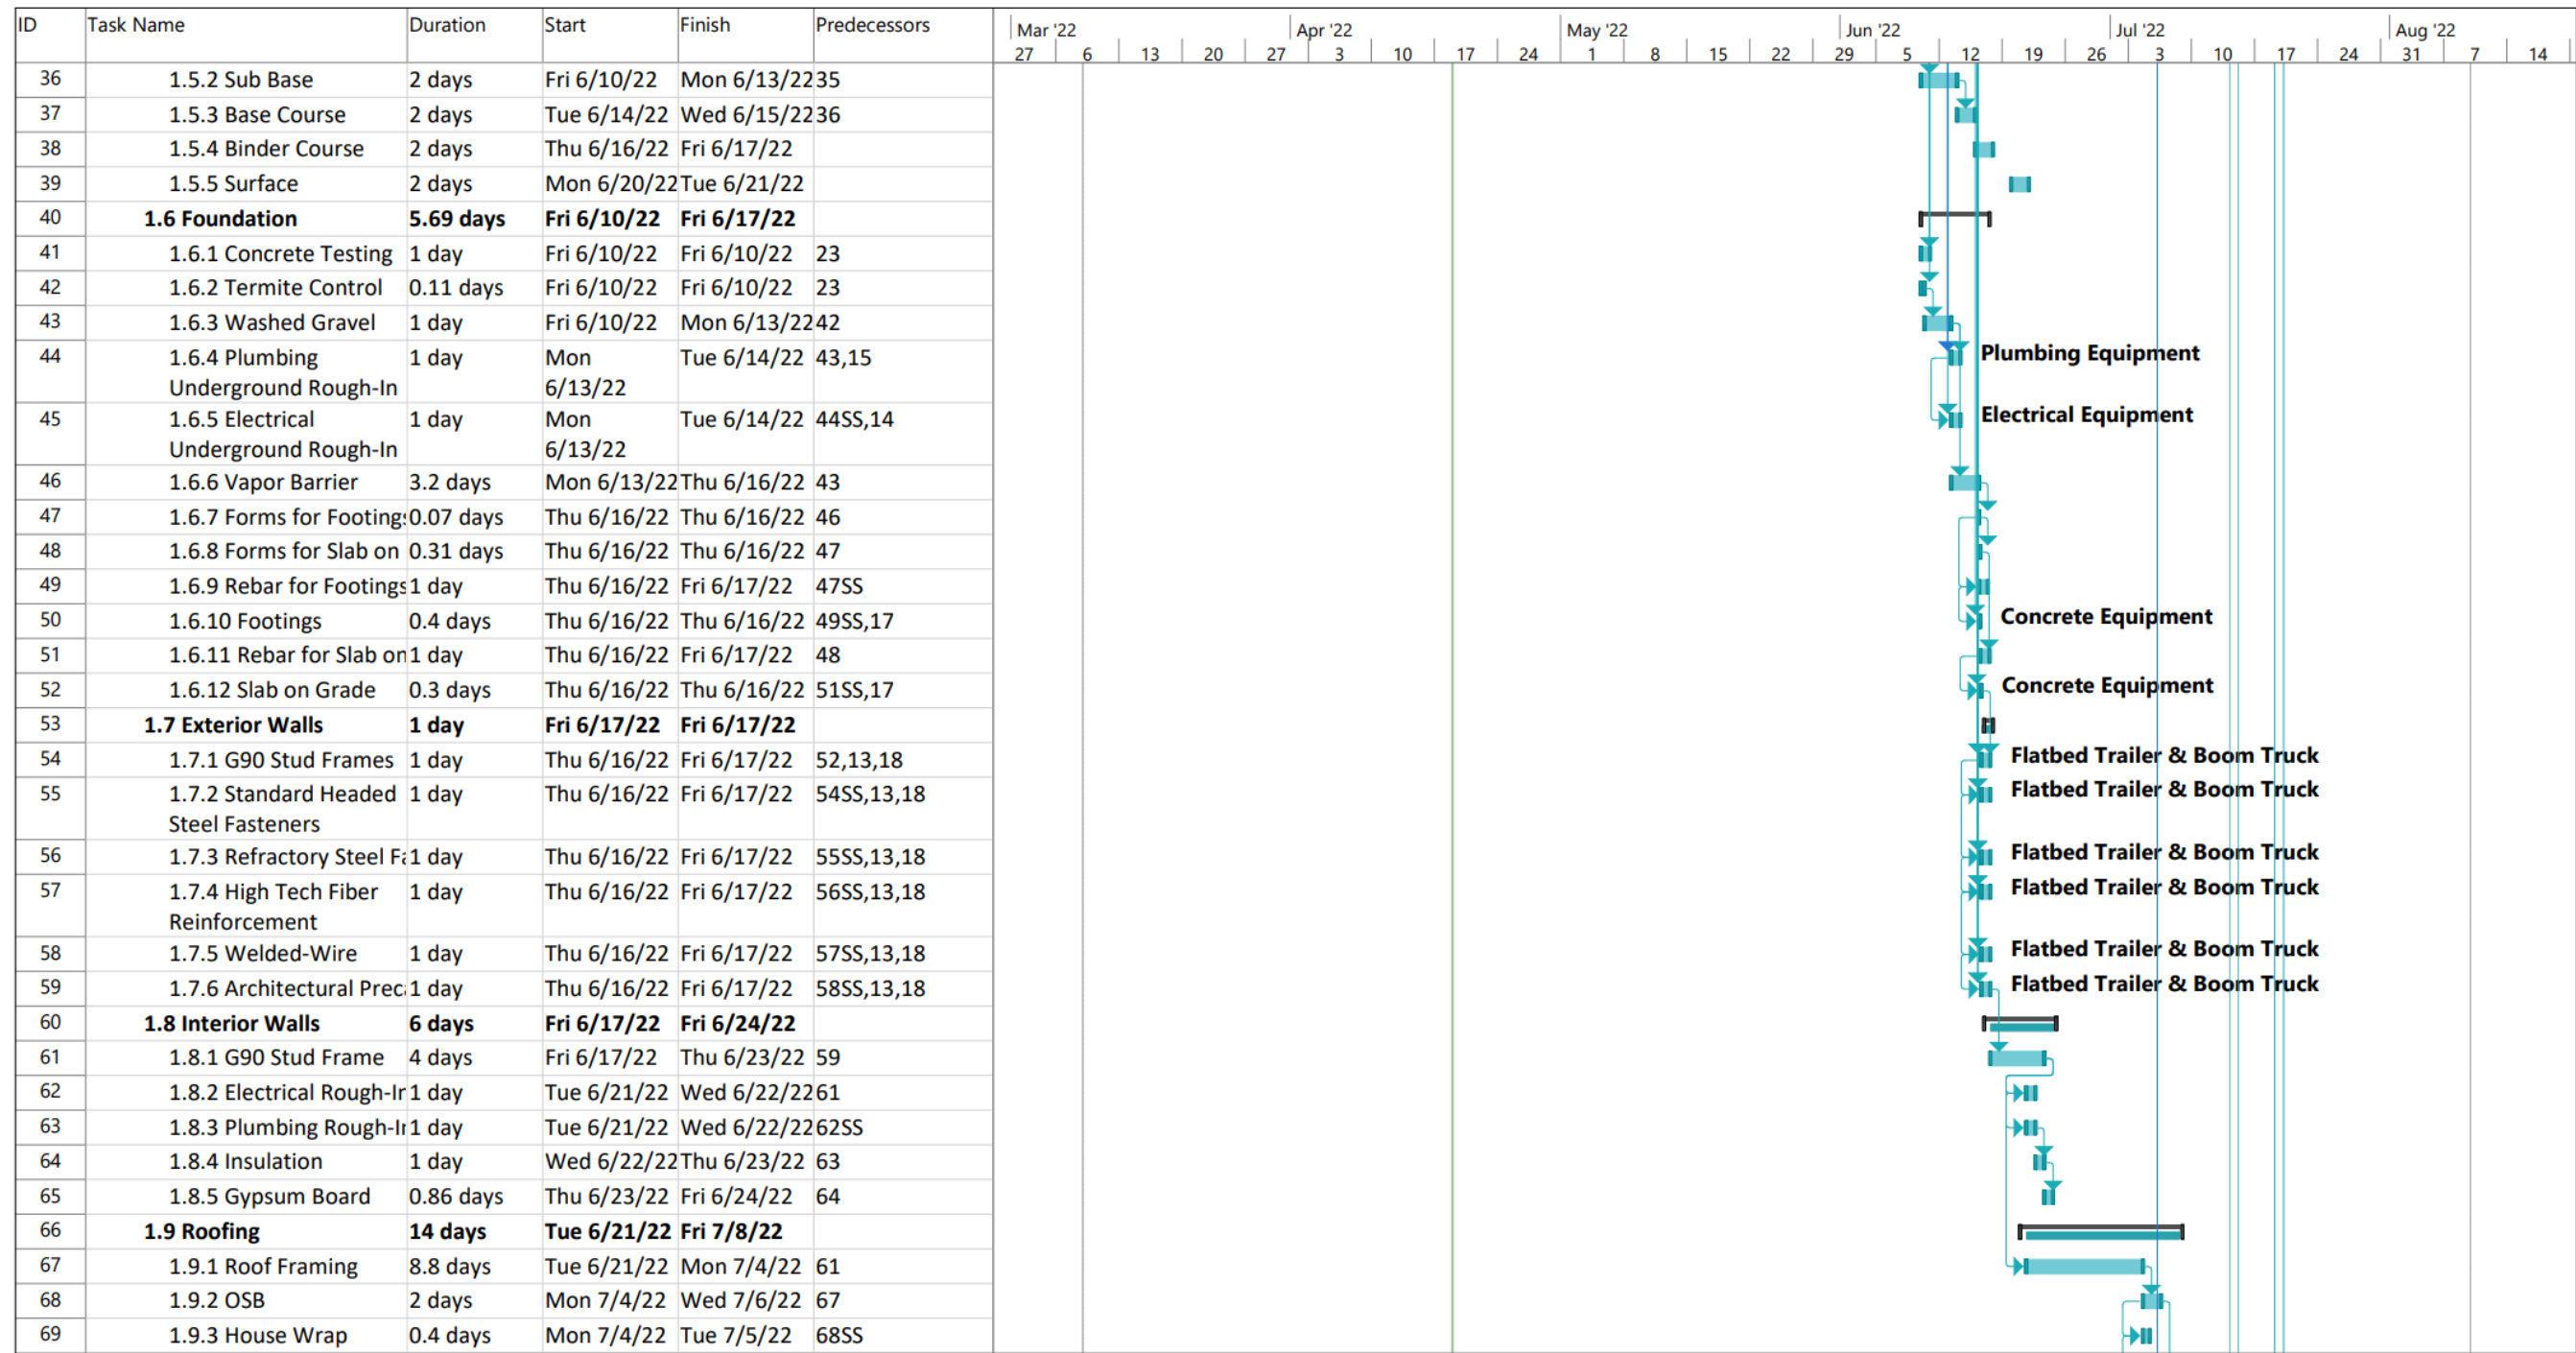

Project: Schematic Design - Sch Date: Tue 4/19/22	Task	Inactive Task	Manual Summary Rollup	External Milestone	Manual Progress
	Split	Inactive Milestone	Manual Summary	Deadline	Critical
	Milestone	Inactive Summary	Start-only	Critical Split	Progress
	Summary	Manual Task	Finish-only	External Tasks	Progress
	Project Summary	Duration-only	External Tasks	Progress	Progress

ID	Task Name	Duration	Start	Finish	Predecessors	Mar '22	Apr '22	May '22	Jun '22	Jul '22	Aug '22
70	1.9.4 Asphalt Felt Paper	2 days	Mon 7/4/22	Wed 7/6/22	69SS						
71	1.9.5 Asphalt Shingles	2 days	Wed 7/6/22	Fri 7/8/22	70						
72	1.9.6 Flashing	2 days	Wed 7/6/22	Fri 7/8/22	70						
73	<b>1.10 Openings</b>	<b>3 days</b>	<b>Fri 7/8/22</b>	<b>Tue 7/12/22</b>							
74	1.10.1 French Doors	0.16 days	Fri 7/8/22	Fri 7/8/22	71						
75	1.10.2 Closet Doors	0.4 days	Fri 7/8/22	Mon 7/11/22	74SS						
76	1.10.3 Interior Doors	0.38 days	Fri 7/8/22	Mon 7/11/22	75SS						
77	1.10.4 Exterior Doors	0.11 days	Fri 7/8/22	Fri 7/8/22	74SS						
78	1.10.5 Windows 1/8" Glass with Flashing	1.3 days	Fri 7/8/22	Tue 7/12/22	77						
79	1.10.6 60x46 Double Hu	1.3 days	Tue 7/12/22	Wed 7/13/22	78						
80	1.10.7 30x46 Double Hu	0.2 days	Tue 7/12/22	Tue 7/12/22	79SS						
81	1.10.8 24x16 Windows	0.38 days	Tue 7/12/22	Tue 7/12/22	79SS						
82	<b>1.11 MEP</b>	<b>7 days</b>	<b>Wed 7/6/22</b>	<b>Thu 7/14/22</b>							
83	1.11.1 Mechanical Roug	4 days	Wed 7/6/22	Tue 7/12/22	68						
84	1.11.2 Electrical Rough-	4 days	Wed 7/6/22	Tue 7/12/22	83SS,14						
85	1.11.3 Plumbing Rough-	4 days	Wed 7/6/22	Tue 7/12/22	83SS,15						
86	1.11.4 Mechanical Testi	1 day	Tue 7/12/22	Wed 7/13/22	85						
87	1.11.5 Electrical Testing	1 day	Tue 7/12/22	Wed 7/13/22	86SS						
88	1.11.6 Plumbing Testing	1 day	Tue 7/12/22	Wed 7/13/22	86SS						
89	1.11.7 Mechanical Inspe	1 day	Wed 7/13/22	Thu 7/14/22	88						
90	1.11.8 Electrical Inspect	1 day	Wed 7/13/22	Thu 7/14/22	89SS						
91	1.11.9 Plumbing Inspect	1 day	Wed 7/13/22	Thu 7/14/22	89SS						
92	<b>1.12 Finishes</b>	<b>5 days</b>	<b>Wed 7/13/22</b>	<b>Tue 7/19/22</b>							
93	1.12.1 Concrete Stain	1.8 days	Wed 7/13/22	Fri 7/15/22	88						
94	1.12.2 Trim	1 day	Tue 7/12/22	Wed 7/13/22	93						
95	1.12.3 Paint	3 days	Tue 7/12/22	Fri 7/15/22	94SS						
96	1.12.4 Light Fixtures	2 days	Fri 7/15/22	Tue 7/19/22	95						
97	1.12.5 Hardware	2 days	Fri 7/15/22	Tue 7/19/22	96SS						
98	<b>1.13 Appliances</b>	<b>1 day</b>	<b>Fri 7/15/22</b>	<b>Fri 7/15/22</b>							
99	1.13.1 Cooking Range	0.1 days	Fri 7/15/22	Fri 7/15/22	93						
100	1.13.2 Refrigerator	0.1 days	Fri 7/15/22	Fri 7/15/22	99SS						
101	1.13.3 Dishwasher	0.25 days	Fri 7/15/22	Fri 7/15/22	99SS						
102	1.13.4 Hood for Range	0.2 days	Fri 7/15/22	Fri 7/15/22	99SS						
103	1.13.5 Washer	0 days	Fri 7/15/22	Fri 7/15/22	99SS						
104	1.13.6 Dryer	0.3 days	Fri 7/15/22	Fri 7/15/22	99SS						
105	<b>1.14 Driveway</b>	<b>4 days</b>	<b>Thu 7/14/22</b>	<b>Tue 7/19/22</b>							

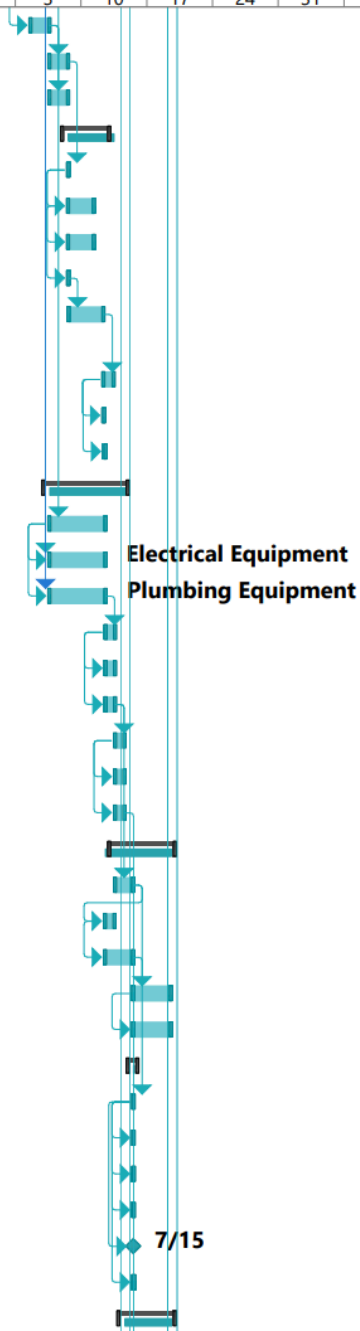

Project: Schematic Design - Sch Date: Tue 4/19/22	Task	Inactive Task	Manual Summary Rollup	External Milestone	Manual Progress
	Split	Inactive Milestone	Manual Summary	Deadline	Critical
	Milestone	Inactive Summary	Start-only	Critical Split	Progress
	Summary	Manual Task	Finish-only	External Tasks	
	Project Summary	Duration-only	External Tasks	Progress	

